

Scaling Up: From Bike Lanes to Complete Networks

Ryan Vanderputten - City of Calgary

Stephanie Shaw - NYC DOT

David Pulsipher - Denver Public Works

Peter Eccles - City of Houston

Geoff Carleton - Harris County Texas


Jessica Zenk - San José DOT (moderator)



197 Miles



345 Miles

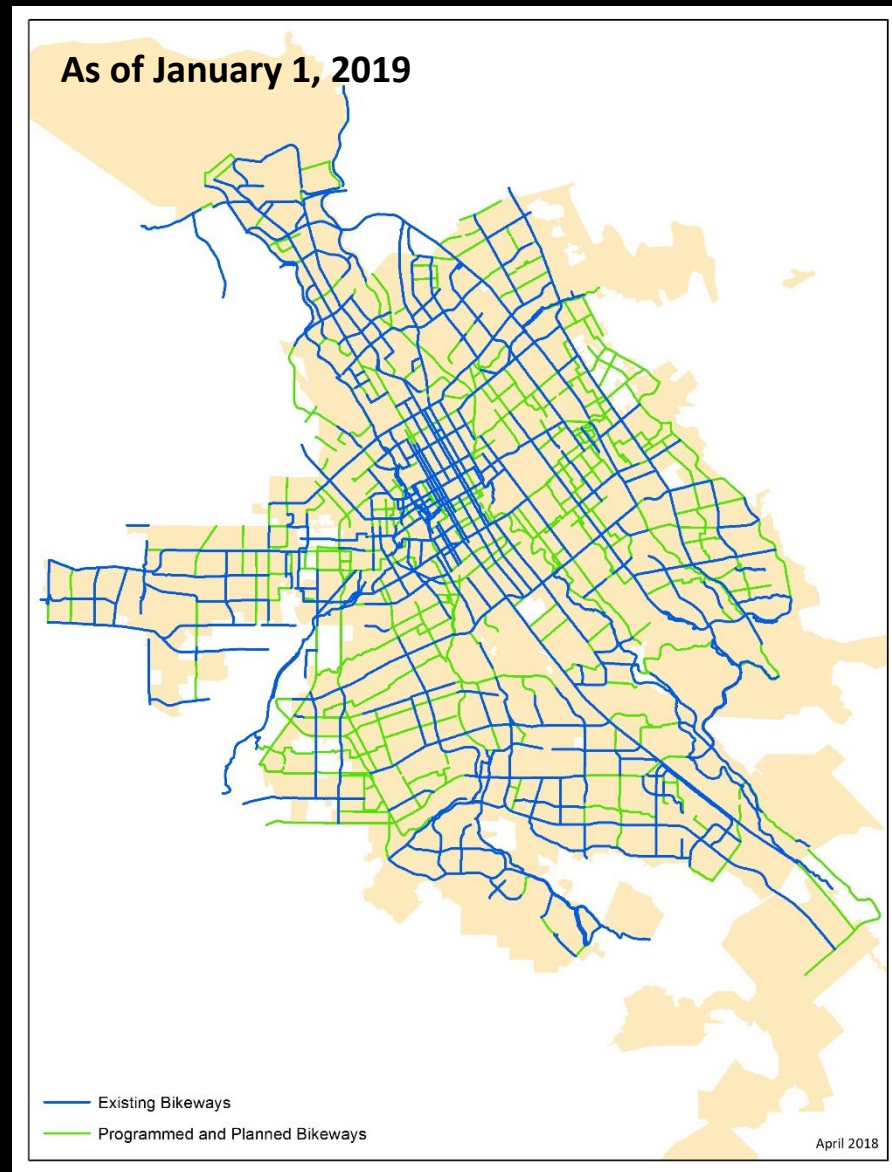

Before



After



WORKPLAN DEVELOPMENT

- PM Proposed Roadways
 - Bike Plan
 - Grant Funded
 - Gaps
- Community Requests

Steps (1 - 4)

PROJECT FEASIBILITY

- Conceptual Review
- Data Collection
- Initial Circulation
- Initial Council Outreach

Steps (5 - 9)


PROJECT DEVELOPMENT

- Develop Plans
- Solicit Input (OPS, NTM, etc.)
- Community Engagement
 - Council Outreach
- Project Revisions (Final Plans)
 - Environmental

Steps (10 - 12)

IMPLEMENTATION


- Construction Coordination
- Project Administration
 - After Studies

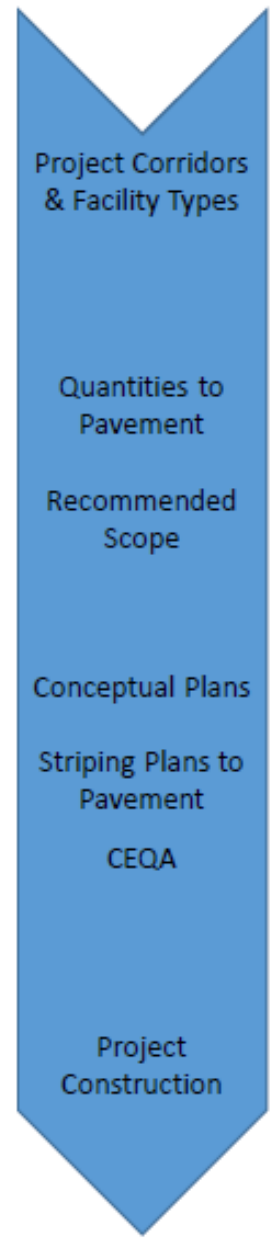

Rapid Implementation of All-Ages & Abilities Network

- Connecting with Trails, Getting Across Barriers
- 2017: Project Launch
- 2018: 10 Miles
 - Protected (5 Miles)
 - Bike Boulevard (3 Miles)
 - Buffered Bike Lanes (2 Miles)
- 2019 & 2020: 12 Miles & Upgrades
- 2021: Civil Changes to San Fernando St.

You're in the network!

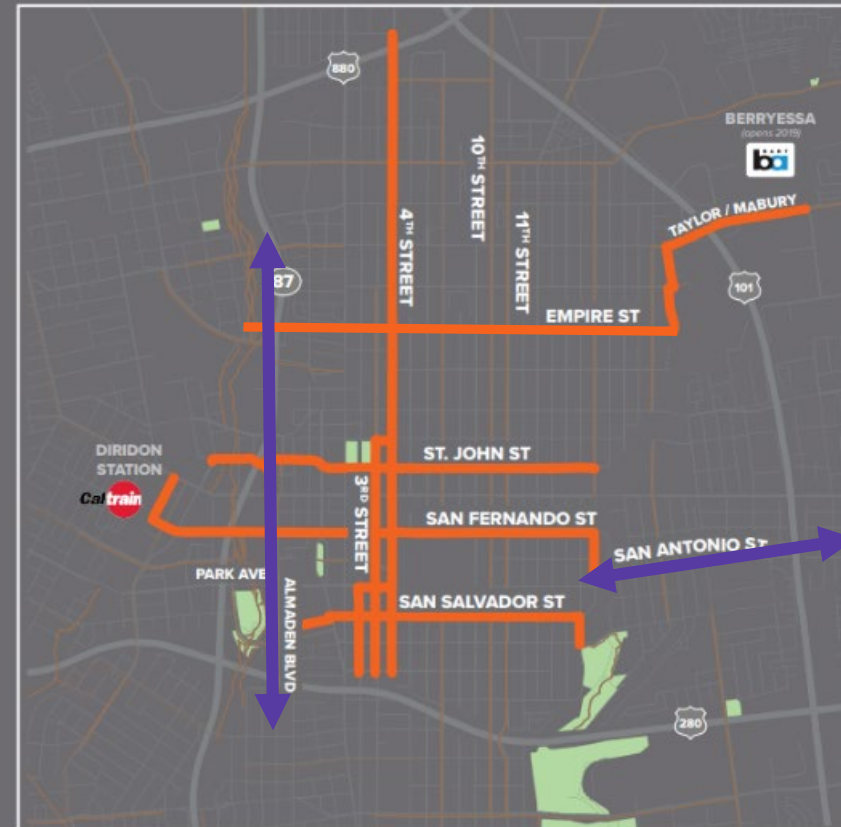


sanjoseca.gov/betterbikeways



SAN JOSE

San Jose DOT Complete Streets Annual Workplan

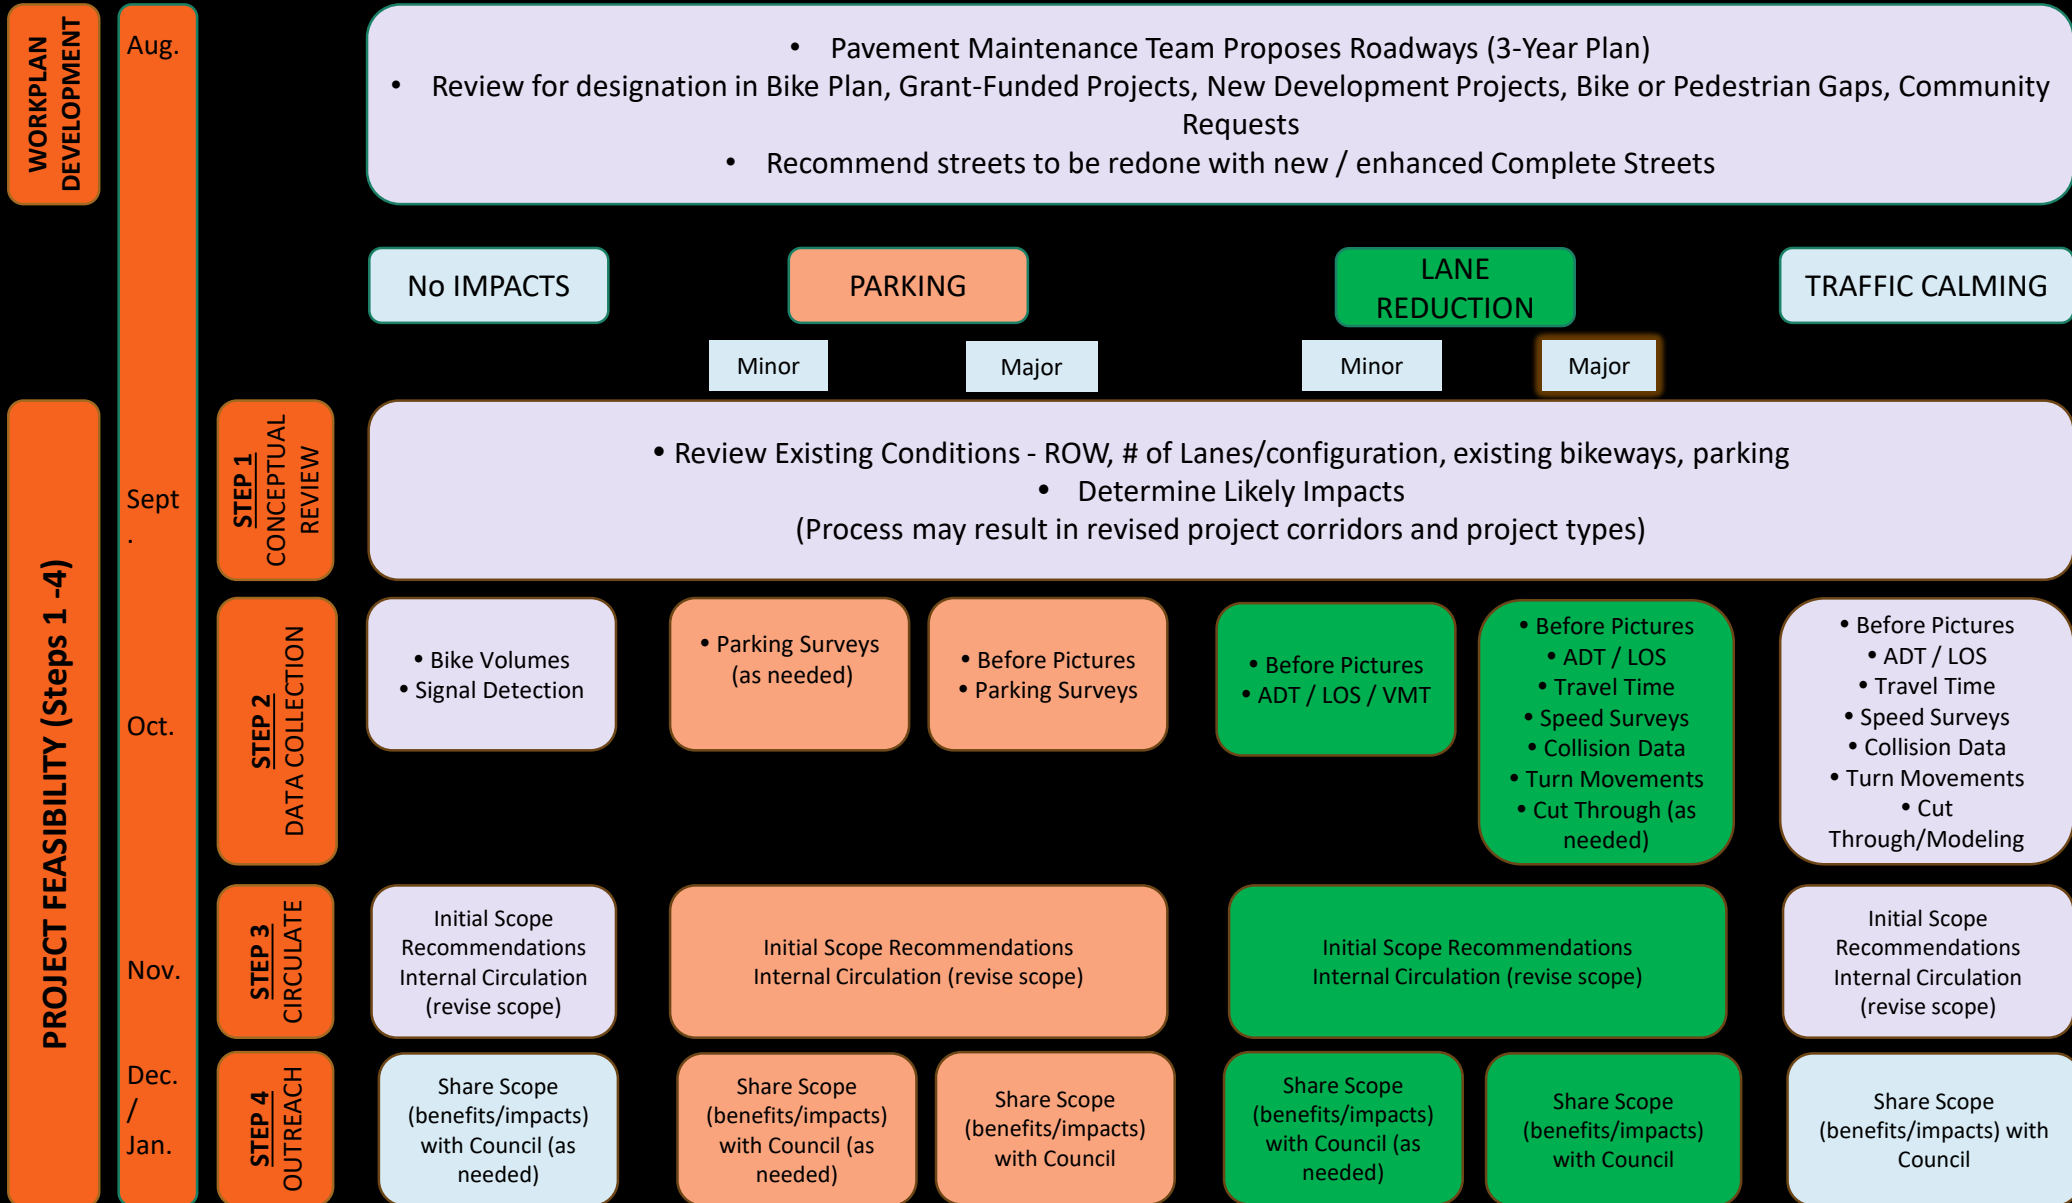

PROJECT DEVELOPMENT (Steps 5 - 9)		No IMPACTS		PARKING		LANE REDUCTION		TRAFFIC CALMING
				Minor	Major	Minor	Major	
		Month	Step	Activity	Activity	Activity	Activity	Activity
Jan.	STEP 5 DESIGN	Standard Details, or design plans (in-house or consultant)	Standard Details, or design plans (in-house or consultant)	Design Plans (In-house or Consultant)	Design Plans (In-house or Consultant) Street Mix Cross Sections		Design Plans Street Mix Cross Sections	
Feb.	STEP 6 CIRCULATION	Internal Circulation (as needed)	Internal Circulation (DOT, Council Offices)		Internal Circulation (DOT, Council Offices)		Internal Circulation	
Mar.	STEP 7 Community Outreach	N/A	Proposed Parking Impact Notification (as needed)	Council Office Notice of Meeting Community Mtgs.	Council Office Notice of Meeting Community Mtgs. (as needed)	Council Office Notice of Meeting Community Mtgs.	Council Office Notice of Meeting Community Mtgs.	
April	STEP 8 REVISIONS	N/A	Mitigate Concerns as Feasible and Revise Plans		Mitigate Concerns as Feasible and Revise Plans		Mitigate Concerns as Feasible and Revise Plans	
May	STEP 9 CEQA	CEQA Exempt (2180.20.5)	CEQA Exempt (2180.20.5)		Project Specific CEQA (15301)		Project Specific CEQA (15301)	

No IMPACTS

PARKING

LANE
REDUCTION

TRAFFIC CALMING

PROJECT IMPLEMENTATION (Steps 10 - 12)

June

STEP 10
Construction
Outreach

- 1 Week Prior to Construction - IM construction flyer (Identifies timeline, temporary impacts and street changes)
- During Construction – Project Display Flyer (shows new configuration and appropriate use of new configuration)

July

Aug

Sept

STEP 11
Delivery /
Coordination

- Communicate community Feedback (issues, complaints) to IM or Contractor
 - Address Design Issues during Construction (i.e., striping and parking)
 - Ensure 100% Project completion

Oct

Nov

STEP 12
Closeout /
Administrative

- Update Bikeway Network Info (DOT Maps, Google Maps)
 - After Studies
 - Grant Admin.
- Evaluate Project Design/Development and Implementation Process for on-going Process Improvement
